
ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		**Phase 1**	**9 days**	**Mon 5/5/25**	**Thu 5/15/25**		
2		Traffic Control- PCMS	1 day	Mon 5/5/25	Mon 5/5/25		Forward Traffic
3		Setup Traffic Control	1 day	Tue 5/13/25	Tue 5/13/25	2FS+5 days	Forward Traffic
4		Southbound Signal Loops	1 day	Wed 5/14/25	Wed 5/14/25	3	Parisi/ Highway Li
5		Setup Traffic Control	1 day	Wed 5/14/25	Wed 5/14/25	3	Forward Traffic
6		Northbound Signal Loops	1 day	Thu 5/15/25	Thu 5/15/25	4	Parisi/ Highway Li
7		Remove Traffic Control	1 day	Thu 5/15/25	Thu 5/15/25	4	Forward Traffic
8		**Phase 2**	**33 days**	**Thu 5/15/25**	**Mon 6/30/25**		
9		Stage 2 Traffic Control Setup	1 day	Thu 5/15/25	Thu 5/15/25	7SS	Forward Traffic
10		Install Erosion Control	1 day	Fri 5/16/25	Fri 5/16/25	9	West-Land
11		Removals	5 days	Mon 5/19/25	Fri 5/23/25	10	Parisi
12		Storm Sewer	5 days	Tue 5/20/25	Mon 5/26/25	11SS+1 day	Parisi
13		Electrical-Bases and Conduit	5 days	Wed 5/21/25	Tue 5/27/25	11SS+2 days	Highway Light
14		Grading	7 days	Thu 5/22/25	Fri 5/30/25	12SS+2 days	Parisi
15		Grading- Tie into Pepsi Way	2 days	Mon 6/2/25	Tue 6/3/25	14	Parisi
16		Curb Prep and Pour	2 days	Wed 6/4/25	Thu 6/5/25	15	Parisi
17		Adjustments	1 day	Fri 6/6/25	Fri 6/6/25	16	Parisi
18		Concrete Pavement	5 days	Mon 6/9/25	Fri 6/13/25	17	Parisi
19		Concrete Sidewalk	2 days	Thu 6/12/25	Fri 6/13/25	18FS-2 days	Parisi
20		Topsoil	2 days	Thu 6/12/25	Fri 6/13/25	16FS+4 days	Parisi
21		Asphalt Pavement	1 day	Thu 6/19/25	Thu 6/19/25	18FS+3 days	Tri-County
22		Restoration	3 days	Fri 6/20/25	Tue 6/24/25	21	West-Land
23		Pavement Markings	1 day	Wed 6/25/25	Wed 6/25/25	22	Forward Traffic
24		Sign Install	2 days	Thu 6/26/25	Fri 6/27/25	23	West-Land
25		Remove Traffic Control	1 day	Mon 6/30/25	Mon 6/30/25	24	Forward Traffic
26		**Phase 3**	**13 days?**	**Mon 6/30/25**	**Wed 7/16/25**		
27		Stage 3 Traffic Control Setup	1 day	Mon 6/30/25	Mon 6/30/25	25SS	Forward Traffic
28		Removals	1 day	Tue 7/1/25	Tue 7/1/25	27	Parisi
29		Prep and Pour Curb	2 days	Wed 7/2/25	Thu 7/3/25	28SS+1 day	Parisi
30		Topsoil and Grade for Asphalt	1 day	Fri 7/4/25	Fri 7/4/25	29	Parisi
31		Asphalt Paving	1 day	Thu 7/10/25	Thu 7/10/25	29FS+4 days,3	Tri-County
32		Restoration	1 day	Fri 7/11/25	Fri 7/11/25	31	West-Land
33		Sign Install	2 days	Mon 7/14/25	Tue 7/15/25	32	West-Land
34		Remove Traffic Control	1 day?	Wed 7/16/25	Wed 7/16/25	33	Forward Traffic
35		**Phase 4**	**5 days**	**Mon 9/15/25**	**Fri 9/19/25**		
36		Setup Traffic Control	1 day	Mon 9/15/25	Mon 9/15/25		Forward Traffic
37		Install Signal Equipment	5 days	Mon 9/15/25	Fri 9/19/25		Highway Light
38		Remove Traffic Control	1 day	Mon 9/15/25	Mon 9/15/25		Forward Traffic

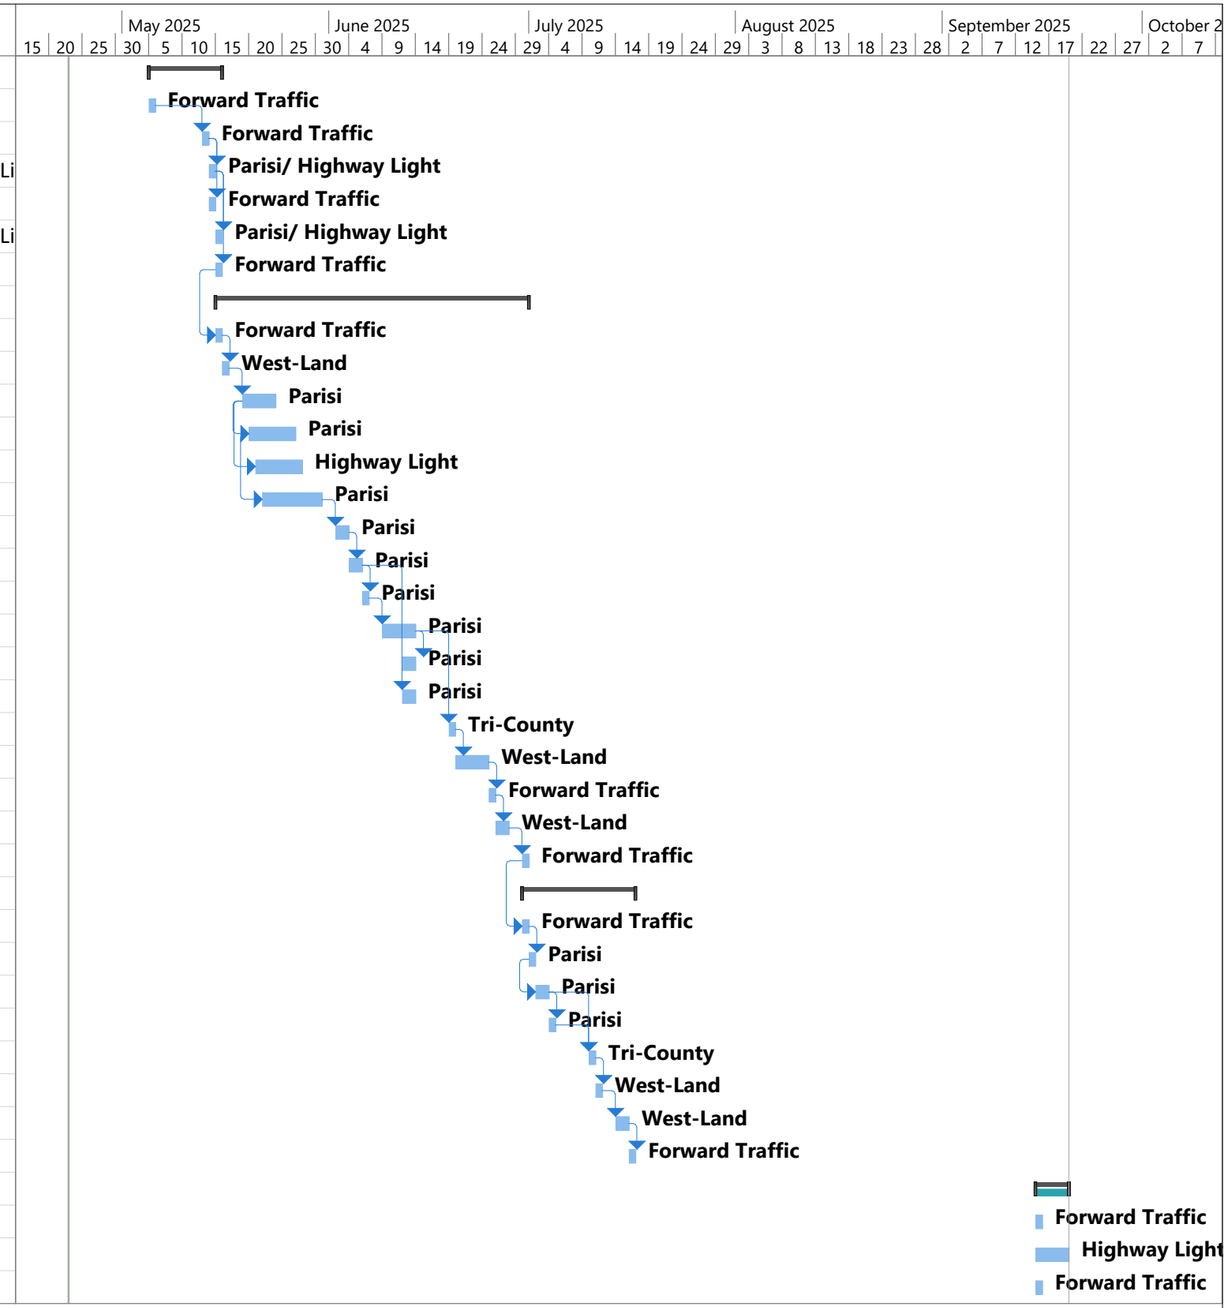

Project: Pepsi way and 51 Initia
Date: Wed 4/23/25

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
